

21 October 2009

Drilling and Seismic Update

WestSide's next phase of drilling and appraisal commences

Current activity

- **Tilbrook:** #9a vertical well commenced.
- **Mount St Martin:** Seismic acquisition completed and crews moving to Tilbrook.
- **Paranui:** Seismic drilling completed ready for acquisition.

Up to 16 wells are planned as part of the 2009 / 2010 exploration program across WestSide's tenements.

ATP 688P coal seam gas drilling program (Tilbrook)

WestSide has commenced a multi well program in ATP 688P in the northern Bowen Basin. The first three wells of the program (Tilbrook #9a, #10a and #10b) are exploration wells to confirm coal in the P seam and Goonyella seams of the Moranbah Coal Measures in preparation for the drilling of two sets of horizontal chevron-style dual-lateral wells (Tilbrook #L9a and #L9b, Tilbrook #L10a and #L10b) which are planned to intersect with new vertical wells (Tilbrook #9 and #10).

Latest activity – Tilbrook #9a

The Tilbrook #9a vertical exploration well has completed surface casing. BOP's are rigged up ready for recommencement of drilling when crews return as planned on 28 October.

Summary : ATP 688P coal seam gas drilling program (Oct – Nov)

Well	Well Type	Spud Date	Finish Date	Current Status
Tilbrook # 9a	Exploration	16 Oct 2009	5 Nov 2009 (Planned)	Surface casing completed ready to recommence drilling after crew break. Well will be set up for further testing.
Tilbrook # 10a	Exploration	8 Nov 2009	20 Nov 2009 (Planned)	Site preparation in progress
Tilbrook # 10b	Exploration	22 Nov 2009	29 Nov 2009	Site preparation in progress

Boart Longyear is the drilling contractor.

Expected operations in the next week

Site preparations will continue at Tilbrook #10a and #10b.

ATP 688P coal seam gas seismic program (Tilbrook and Mount Saint Martin)

WestSide is conducting a seismic acquisition program in the Tilbrook and Mount Saint Martin areas of ATP 688P. Seismic data will be acquired over two 5km lines.

Latest activity

Seismic acquisition was completed over a 5km length at Mount Saint Martin and has commenced at Tilbrook.

Summary : Seismic program

Area	Type	Start	Finish Date	Current Status
Mt St Martin	5 km of Viborseis	19 Oct 2009	21 Oct 2009	Data acquisition completed
Tilbrook	5 km of Viborseis	22 Oct 2009	24 Oct 2009 (Planned)	Acquisition stage
Paranui (ATP 769P)	10 km of dynamite seismic	TBA	TBA	Drilling completed. Awaiting crews for acquisition

Expected operations in the next week

Seismic acquisition will take place over a 5km length at Tilbrook.

About WestSide Corporation Ltd

WestSide Corporation Limited is listed on ASX (ASX code: WCL) and has interests in coal seam gas (CSG) projects in Queensland and Indonesia. WestSide has a 50% interest in ATP 688P and ATP 769P with QGC holding the other 50%.

WestSide is currently operating an appraisal program in ATP 769P (Paranui) and ATP 688P (Tilbrook, Mount Saint Martin and Bald Hill) sites in Queensland's Bowen Basin, and is also assessing the CSG potential of certain coal deposits in Indonesia through its relationship with PT Bumi Resources TBK, one of Indonesia's largest coal miners.

Regular updates will be provided during the course of the drilling campaign.


Additional information is available on WestSide's website: www.westsidecorporation.com.

For further information contact:

WestSide Corporation Ltd
 Angus Karoll
 Chairman and Acting CEO
 07 3020 0900

Media
 Anna O'Gorman
 Principal Consultant - Three Plus
 07 3503 5700
 0423 463 548

Tilbrook CSG Pilot Area

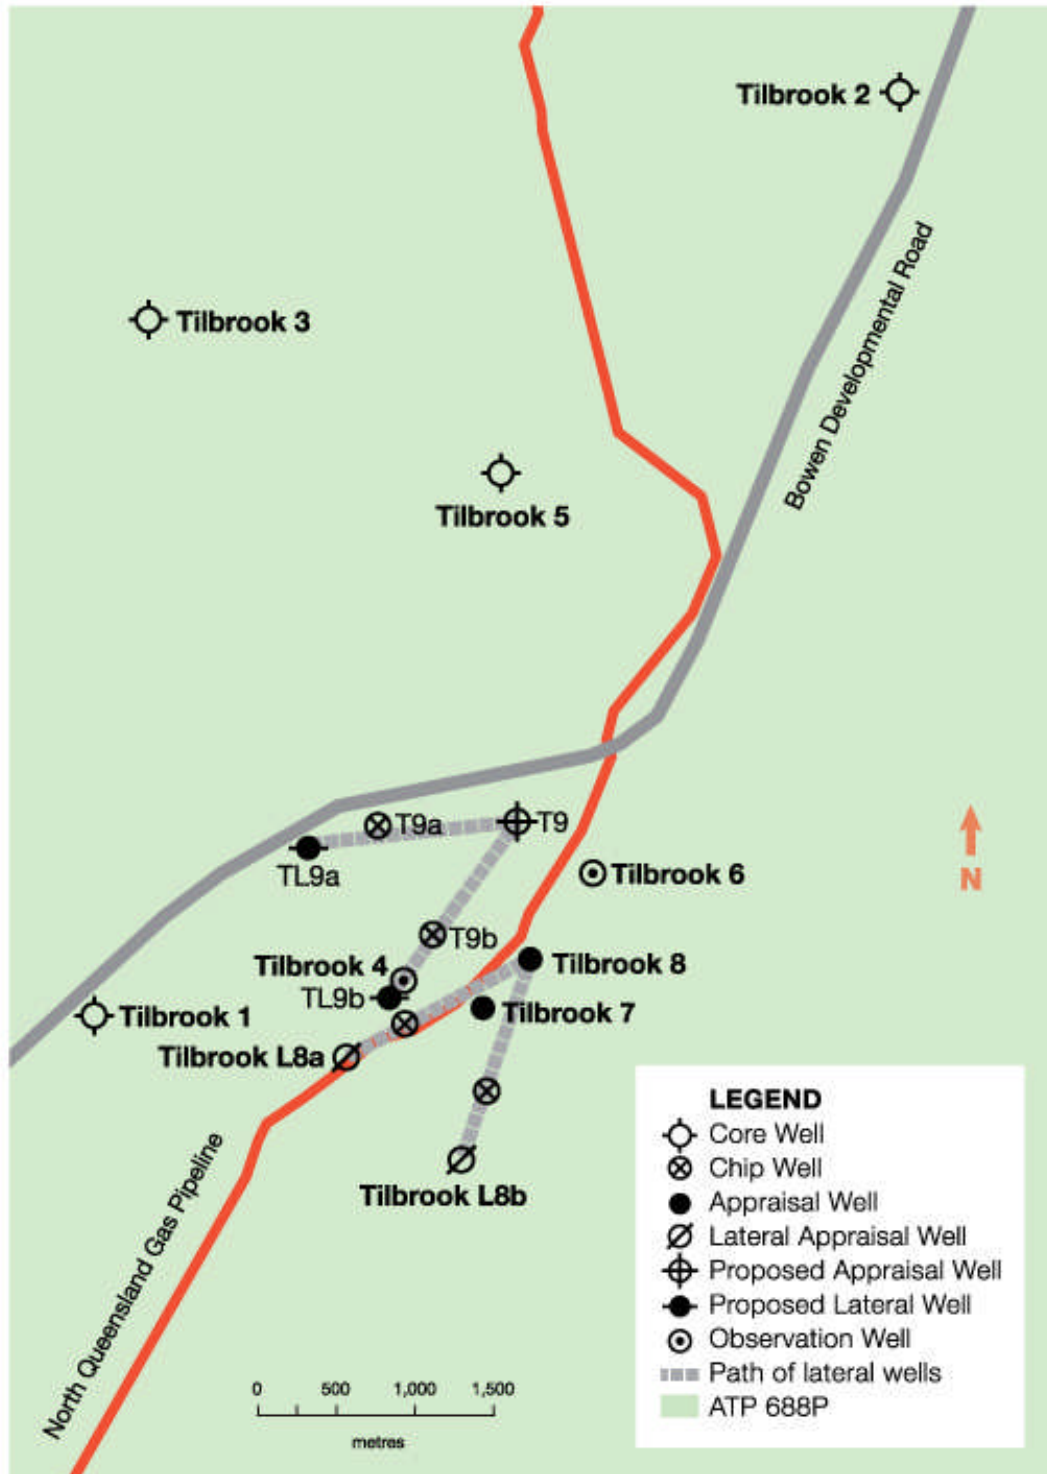

ATP 769P Area of Operations (Paranui)

